

Kevin Richards Memorial Oval Hardcourt and Shade

Troy Newick, Manager City Projects & Engineering

City Projects and Engineering

September 2026

OFFICIAL




Hardcourt & Shade

Stage 4

Project Overview

Location	Kevin Richards Memorial Oval, Millars Well
Current Status	Design Phase
Estimated Cost	\$16M
Importance	Identified shortage in available facilities
Construction commencement target	Mid 2027

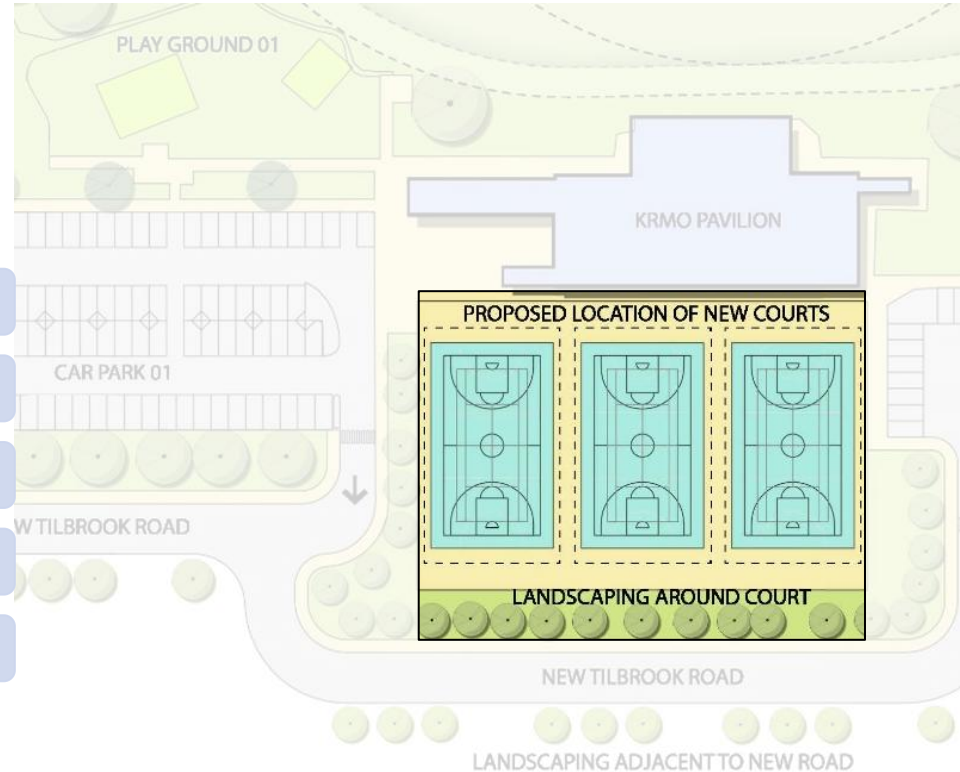

Progress to date

Concept & Schematic completed

Geotechnical investigations completed

Detailed Design completed

Engaged with community and sporting groups completed

Procurement documentation being finalised


Completed Engagement

Who	When	How	What
Netball WA	April 2025	Direct email	Feedback used to determine E/W orientation
Sports groups, clubs and associations	April 2026	Direct email communication	Feedback received on court colour selection, lessons learned from playing at KLP and need for storage
City of Karratha Community	April 2026 – May 2026	Online Survey	Feedback confirmed basketball/ netball as the primary user groups and the design of the hills – 3 colour option
Surrounding residences	May 2026	Direct letter	Provided opportunity for those to attend the information session and provide input in the survey
City of Karratha Community, sports groups, clubs and associations	12 May 2026	Information session	Basketball and netball identified as the primary intended user groups, with no feedback received from tennis or pickleball users. Seating and storage identified


Planned Communications

Who	When	How	What
Nearby Residents Identified key stakeholders	October	Letter Email	Informing of confirmed design, Tender release, and potential construction dates. Opportunity to provide the input into construction requirements
General public	October	Facebook	Informing of design and Tender release
Nearby Residents Identified key stakeholders	February	Letter Email	Inform of Tender Outcome, construction timeline and contractor details
General public	February	Facebook	Inform of Tender Outcome and construction timeline
Nearby Residents Identified key stakeholders	Prior to starting on site	Letter Email	Inform of construction details, access requirements, contractor contact details

Procurement and Construction Timeline

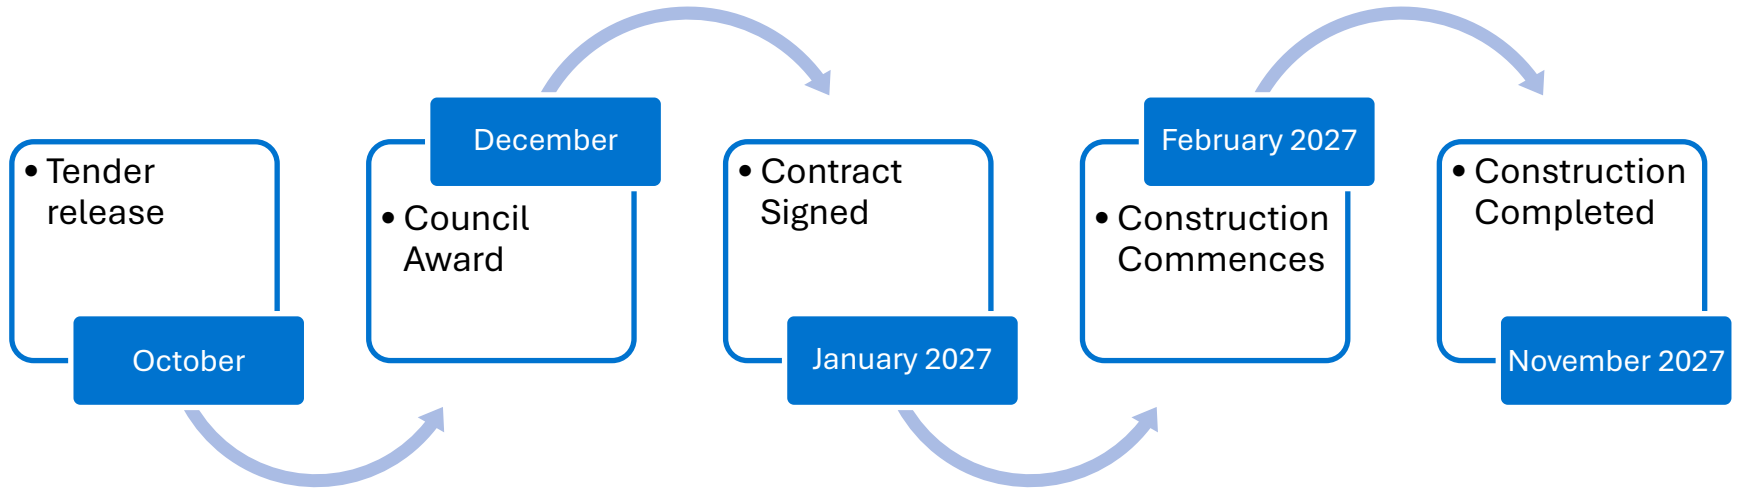

Court Markings

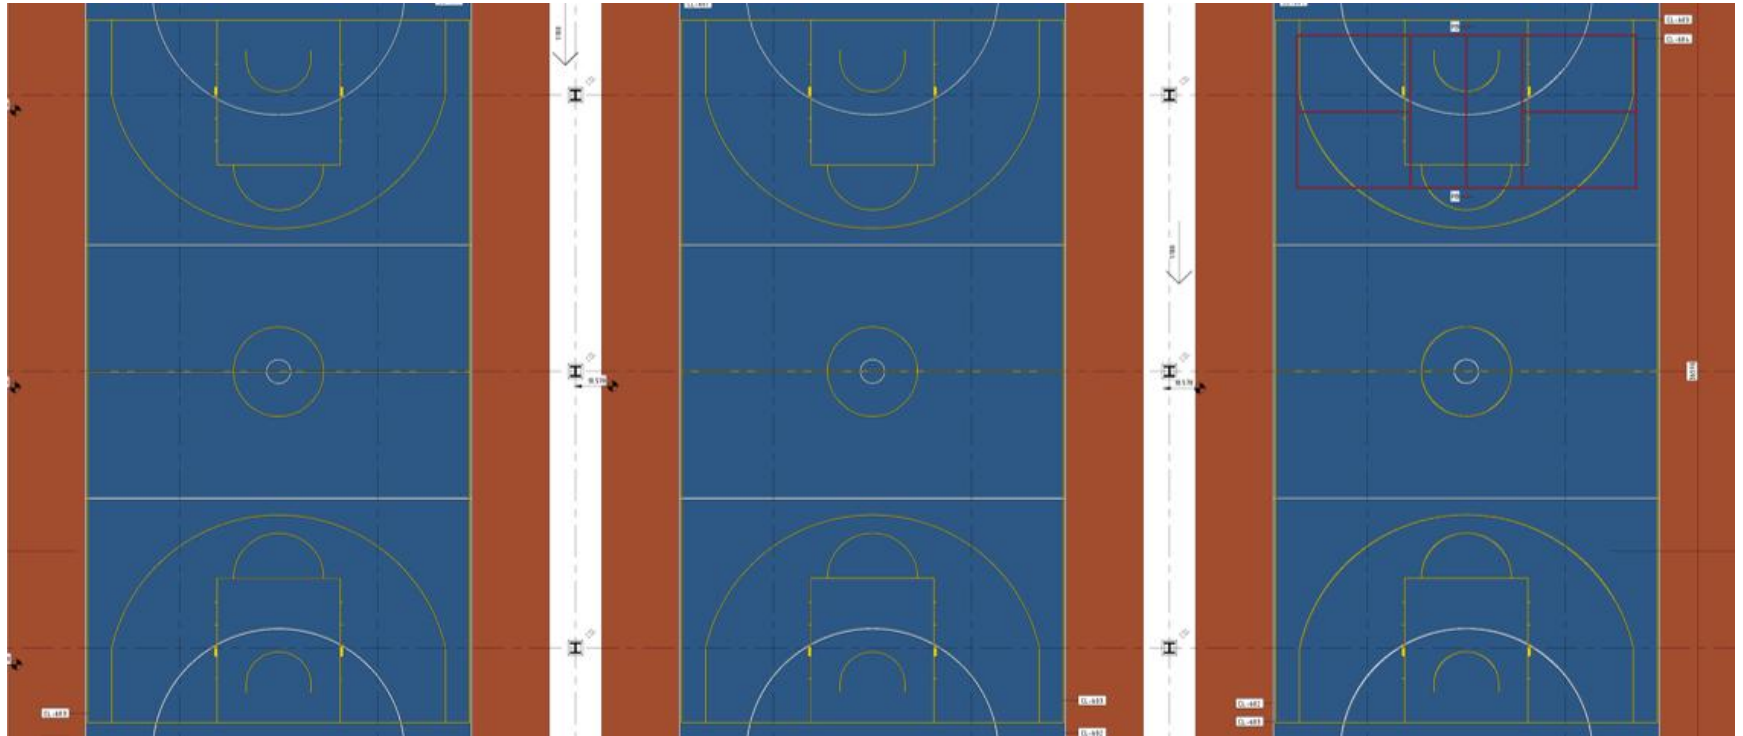



OFFICIAL

For more information:

Troy Newick

Manager City Projects and Engineering

Troy.Newick@karratha.wa.gov.au
